Is it's final bill

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

67208

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of work:- providing & Construction of C.C Road Prashantha Nagara 4th Cross. near S Ramesh Road at Basavahalli in ward No-15.						
	Estimate Cost:- RS 25.00 lakhs						
	Job Code :- 015-18-000024,	P-Code - 1771					
	N.O No:- EE/DD/WO/254/17-18,	Dt. 28.02.18.					
	A.A No:- EE/DD/AS/568/17-18,	Dt. 29.11.17.					
	T.S No:- EE/DD/TS/ 323/17-18,	Dt. 12.12.17.					
	Tender Notification No:- BBMP/EE/DD	Tun/05/ 17-18, Dt. 04.12.17.					
	Agency:- Sri Naveen.T.						
	Recorded on:- 16/8/18.						

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
Item No:-1	Earthwork excavation by manual means in Ordinary Soil involving an average horizontal throw upto 2 metres & an average lift upto 0.5m excavated surface dressed after shaking of clods complete as per specifications.						
	qty brought from this MB page No :- 67295					qty ⇒ 298.32 cum	
	@ RS		87.78	/cum			26187.00/-
Item No:-2	Removing B.S Slab of drain & Stacking etc. Complete.						
	qty brought from this MB page No :- 67295/1					qty ⇒ 120.96 Sqm	
	@ RS.		66.37	/Sqm		———	8028.00/-

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

67209

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Number	Dimensions		Depth	Contents	Reference to last Measurement
			Length	Breadth			
1	2	3	4	5	6	7	8
	Item No:-3 providing & laying in position plain cement concrete of mix 1:4:8 with OPC cement @ 180 kgs, with 40 mm & down size graded granite metal coarse aggregates @ 0.85 cum & fine aggregates @ 0.5 cum. machine mixed curing complete as per Specifications.						
	aty brought from this mB page No:- 67296/1 carried over:-				aty = 149.16 cum		
	Executive Engineer, Karnataka Rural Infrastructure Development Limited, Bangalore.	@ Rs. 5210.99/cum					777137.00/-
	Item No:-4 Cement concrete pavement construction of un-reinforced plain cement concrete pavement, thickness as per design, over a prepared sub-base						

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

67213

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Item No:-10 Disposal of debris to the final place of disposal with all lead & lift & as direction by the engineer in charge of the work lead 412m.						
	i) Add loading & unloading.						
		aty vide Item no-1					
		@Rs. 86.50/cum			aty ⇒ 298.32cum		25805.00/-
					Total bill amt ⇒		2403954.00/-

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಹೆಚ್.ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿಬಿಎಂಪಿ
ಬೆಂಗಳೂರು

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

Certificate:-

1) This is certify that the contractor has completed the work satisfactorily
2) The contractor has cleared the debries from the work spot
3) There are NO adipartmental issues for the above work

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಟಿ.ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿಬಿಎಂಪಿ
ಬೆಂಗಳೂರು

Scanned by CamScanner

M. A. R. 57 (Rule 116) No. D

Measurement Book

67214

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	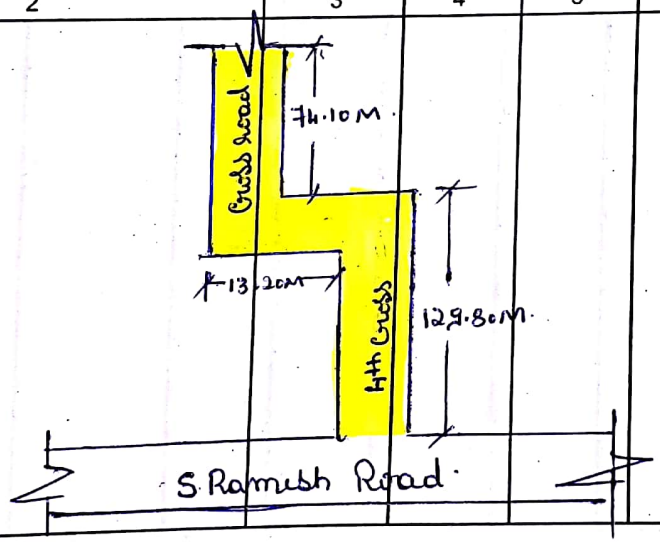						

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಟಿ.ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿಬಿಎಂಪಿ
ಬೆಂಗಳೂರು

Scanned by CamScanner
